


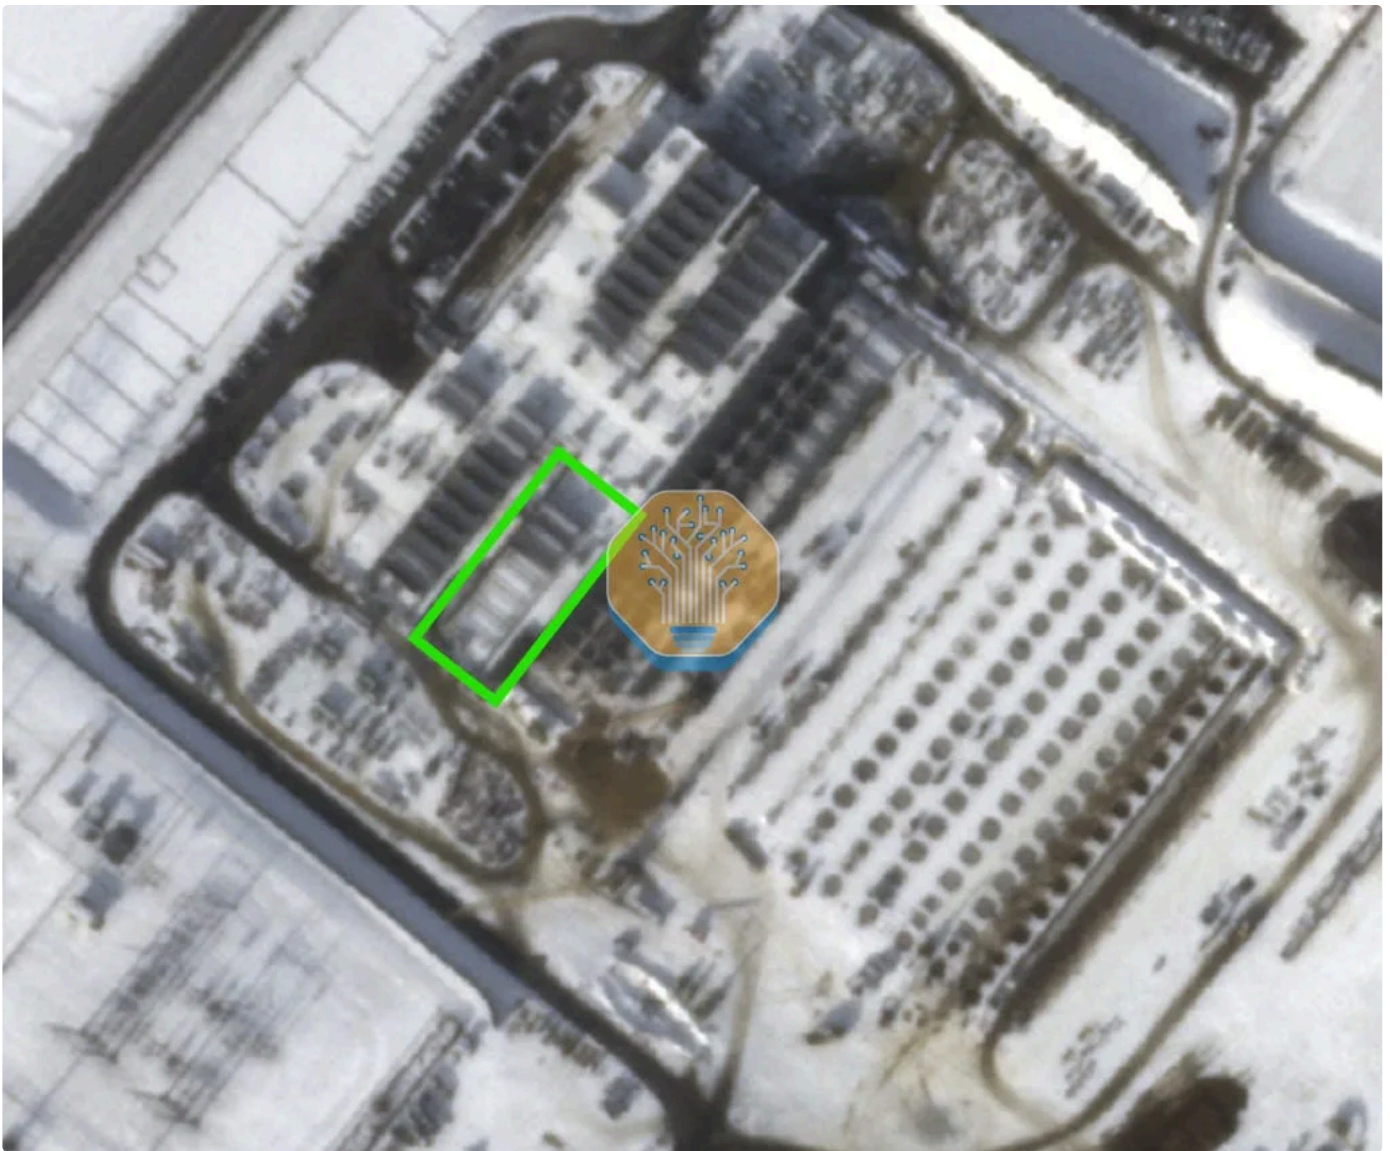

Source: SemiAnalysis Datacenter Industry Model; DataOne/Nebius New Jersey, December 15th, 2025

Putting the full sequence together makes the slippage easy to see (timeline from DataOne's own public disclosures, Nebius earnings calls, and our satellite tracking):

- **March 2025:** targets set at announcement, per the DataOne CEO's public posts, later echo'ed by Nebius. 25 MW by July, 50 MW by September, 100 MW by year-end 2025.
- **June 2025:** first delay acknowledged publicly, delivery pushed to August.
- **September 2025:** the 50 MW building declared imminently delivered, 4 months becoming 6. Our satellite imagery shows only the first batch of chillers, enough for 25 MW, going onto the roof that month.
- **~October 2025:** first 25 MW delivered, seen by the installed chillers.
- **Mid-December 2025:** our December 15th capture shows the second batch of chillers still being installed. Roughly 25 MW energized against the 100 MW promised for year-end.

- **January or February 2026:** full 50 MW complete on our estimates, much later than the targeted 4 month delivery. To be clear, a 10-11 month delivery is still very fast relative to industry standards - so congratulations to Nebius and DataOne.

To understand whether the site will be on time for 2026 delivery and Nebius meet its ARR guidance of \$7-9B by year-end, check our Datacenter Industry Model.



Source: SemiAnalysis Datacenter Industry Model; DataOne/Nebius, New Jersey, as of April 15, 2026

Core Scientific's Denton Campus

Shown in our graph as one of the newer operators with impressive plans, Core Scientific ran into issues that an experienced operator would have likely accounted for when projecting timelines. Let's walk through a quick timeline.

1. In 3Q2024 earnings, they planned to "begin delivery of powered infrastructure for HPC hosting by the **end of the first half of 2025**". This was in reference to all CoreWeave contracted locations, including Denton.

2. 4Q2024, they planned to expand Denton by 70MW, but also saw a delay coming: "These factors introduced several permitting challenges, which we resolved in collaboration with CoreWeave." CORZ now guided 250MW delivered to CoreWeave **by end of 2025**.
3. In addition, infrastructure redesign due to GB200 redesign issues were cited as delay reasons. These reasons had become **very** well-known in the neocloud world.



Adam Sullivan
CEO, President & Director

22:53

Yes, of course. And you're absolutely right on that last point there. As we are evaluating the infrastructure development for the GB200s and the GB300s, there are some incremental design changes that are required as part of that process. And as we've gone -- as we went through really Q4 of last year, there was some incremental permitting challenges. Some of that was driven by the increase in complexity and size. Other parts were for other sites, we had to go back and just reconfirm permitting based on the fact that supply chains are constrained as you look out into 2026. And one of the things that we wanted to ensure that we achieved was that we had the right equipment on the right schedules for the site plans that we had. And so that required us to change some of the designs to fit for the equipment that was available to deliver on the time lines that we set forward. And so there was just some incremental delays there. But overall, we have high confidence in where the delivery schedule that we put forward today, and we believe we're going to be able to hit those time lines.

Source: Core Scientific Earnings, 4Q2024 3. Their 2Q2025 10-Q then vaguely stated delays were arising due to weather and construction, and further pushing timelines out to end of 2025.

1. Moreover, we suspect supply chain challenges partially came from a transformer exploding.

Couple this with satellite imagery of a multiple buildings with no chillers installed, this was clear that the 250MW by YE2025 timeline was going to be missed.
