



Source: SemiAnalysis Datacenter Industry Model; Core Scientific, Denton, Texas, October 29, 2025

Following this, we promptly informed our clients that we see delays coming for CoreWeave.

November 10, 2025

CoreWeave Preview: Short-Term Delays, RPO Strength // Multi-Vertical Note

4 minutes

By Reyk Knuhtsen, Jeremie Eliahou
Ontiveros and Daniel Nishball



Source: SemiAnalysis Datacenter Industry Model; An update regarding CoreWeave's earnings

These challenges are not always avoidable, but experienced operators typically account for them in both timeline and budget.

3. Well-Capitalized Projects Facing Permitting and Local Opposition Issues


Oracle/STACK New Mexico: Permits, a Pipeline, and Pushback

Rather than waving our hands about “regulatory challenges,” let’s detail another project in specific: the STACK Infrastructure/Oracle location that we have delayed to 2029. **The following information was published to our Energy Model and Datacenter Model clients, of which the Energy Model is available as a \$0 bundle for limited time.** Oracle’s June 10 earnings call guided 1H2027 customer

delivery for this campus: a timeline FERC records do not support, nor our estimated construction timelines.

Three things went wrong here. The project tried to thread permitting limits with a two microgrid design, each sitting very close to the major-source threshold. It required a large infrastructure buildout, including a brand new gas pipeline. And organized local opposition slowed every step along the way.

In our March Datacenter Model note, we flagged the Oracle/STACK New Mexico Stargate campus (Project Jupiter, in Doña Ana County) with a delay due to its onsite power system was neither finally permitted nor solidified. The entire campus depends on two behind-the-meter gas microgrids, East (NSR 10732) and West (NSR 10734), filed with the New Mexico Environment Department by Acoma, LLC. NMED received both applications on November 17, 2025 and ruled them complete on January 22, 2026, but each microgrid was being squeezed in as an individual PSD-minor source rather than one major source.

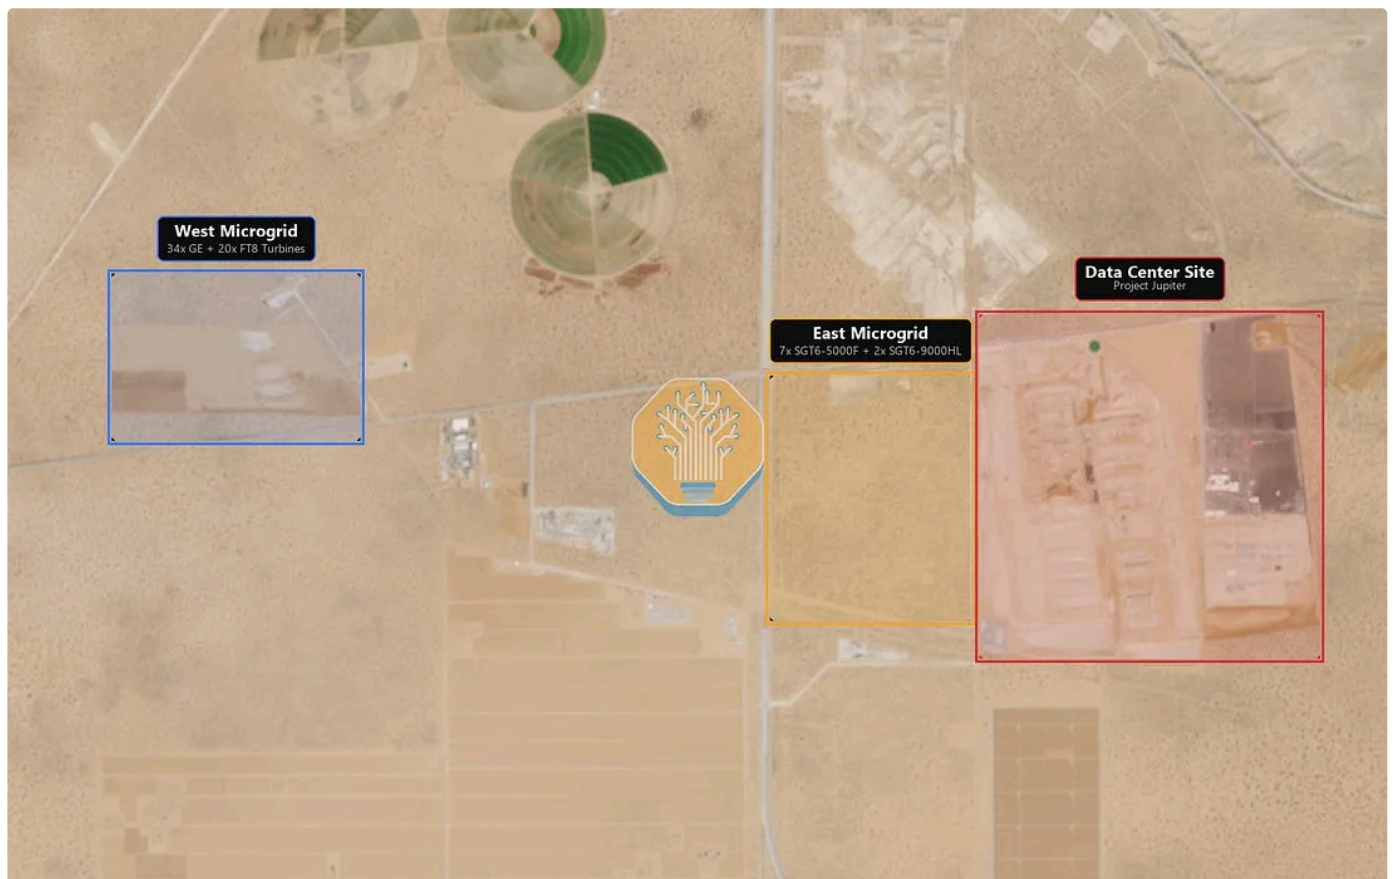

Source: SemiAnalysis Datacenter Industry Model

NMED's December 2025 incompleteness letters found East could emit up to 521 tpy NO_x against a requested 248.90 tpy cap and West up to 388 tpy against 249.97 tpy, both too close to the 250 tpy major-source threshold to be enforceable. On March 23, 2026, NMED pushed both reviews from the April 22 target to July 21, 2026, ordered a public hearing, and cited roughly 7,155 comments plus the applicant's

intent to imminently amend the filings, leaving the public schedule of Q4 2025 construction and Q4 2026 operations untenable.


Meanwhile, the onsite gas generation systems had still not been locked in. In the West Microgrid, for example: “These thirty-four (34) turbines will consist of a combination of GE TM2500 and Mitsubishi FT8 natural gas fired turbines **depending on availability for purchase.**” Depending on availability for purchase with turbine lead times extending multiple years did not make a great case.

⁵ There will be thirty-four (34) turbines at this facility. These thirty-four (34) turbines will consist of a combination of GE TM2500 and Mitsubishi FT8 natural gas fired turbines depending on availability for purchase. The maximum number of each type of units, thirty-four (34) GE TM 2500 and twenty (20) Mitsubishi FT8, are presented in this application. Additional explanation on the configuration of turbines is presented in Section 3 of this application.

Source: Local Filings

Our Energy Model note “Oracle’s New Mexico Stargate Gas Pipeline Delayed: No Bloom Without Gas” published in May found new developments. With the gas turbines unable to clear permitting in time, Oracle withdrew the East and West turbine applications on April 27, 2026 and filed for Bloom Energy fuel cells instead, targeting ~37 tpy NOx. However, this didn’t solve the binding constraint: the 400,000 Dth/d of gas to arrive in **one unprepared pipeline.**

A September 2025 precedent agreement between Green Chile Ventures (likely Oracle subsidiary) and Transwestern baked an August 15, 2026 in-service date into the contract, and Transwestern filed the Green Chile Pipeline at FERC (CP26-80-000) on January 29, 2026 seeking an expedited blanket certificate. That route ran into compounding obstacles: on March 20, the New Mexico State Land Office denied right-of-way across state trust land, forcing a reroute, and on April 13, 2026 FERC staff filed its own protest over the missing New Mexico State Historic Preservation Office (SHPO) sign-off while multiple environmental intervenors filed to intervene, starting a 30-day cure window.

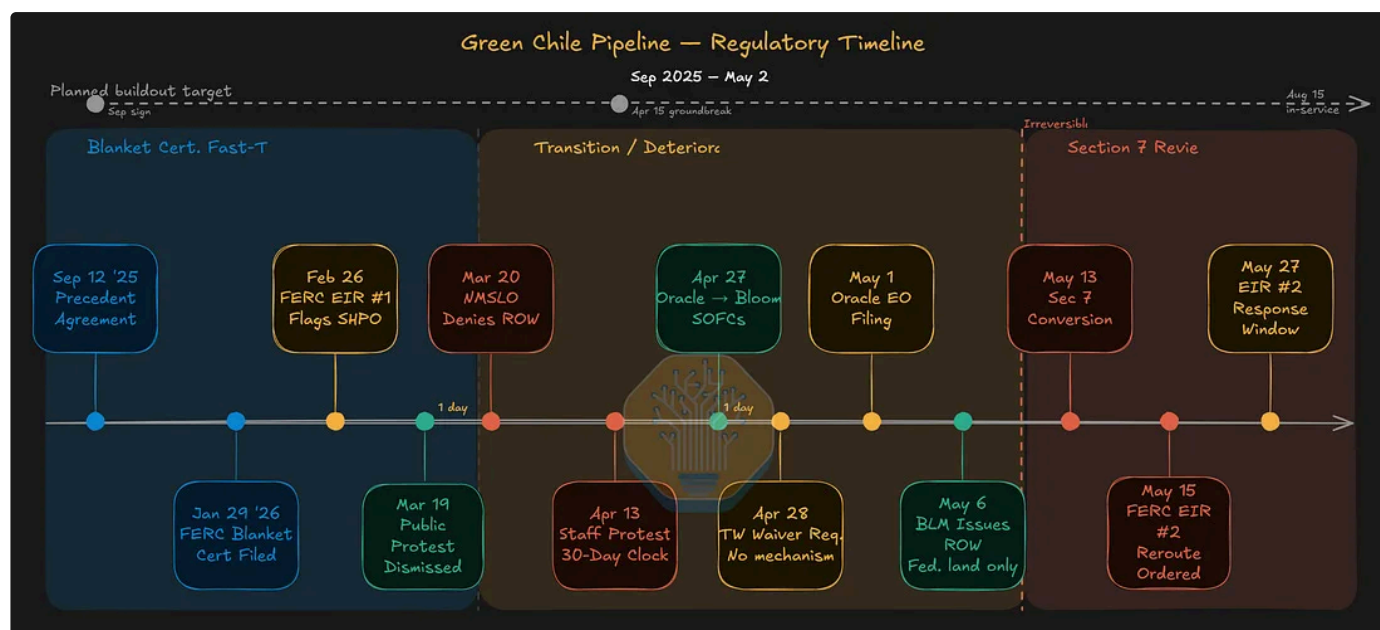

Source: SemiAnalysis Energy Model

Oracle and Transwestern's May 1–4 attempt to extend the cure deadline went nowhere, the window lapsed on May 13 with no SHPO clearance, and on May 15 FERC's Office of Energy Projects opened a formal Section 7 review demanding a full alternative-route analysis avoiding state lands. Transwestern's subsequent sworn filings confirmed no viable alternative route exists and no path around Section 7. The contractual August 15 in-service date became infeasible, and our base case moved first power off 2027 entirely and out to 2029.

NIMBYism rarely kills a capitalized project of this scale outright, but adds months to permits, hearings, and rights-of-way, enough to delay a project past strict deadlines and into large consequences.

What Is Fueling All This Panic?

If those are what real delays look like, the headlines driving the narrative look very different. Most of what circulates as evidence of a datacenter pullback falls into three buckets: moratoriums, organized local opposition, and announcements with timelines that were never realistic to begin with. None of them survive contact with the actual pipeline.

Moratoriums

A datacenter moratorium is a legislative freeze on new construction permits, designed to give jurisdictions time to assess environmental, energy, and economic impacts before approving more capacity. As of April 2026, at least 12 states have filed moratorium bills, and Indiana alone has at least four counties (Fulton, Marshall, Putnam, and White) that have enacted them. These make for alarming headlines until you look at what they actually cover: none of them had datacenters, and we had nothing in our model beyond early stage.

The most dramatic example is Maine, where the Governor vetoed LD 307 in April, which would have been the first statewide datacenter ban in the US. A statewide ban sounds like ominous for the buildout, **except Maine has less than <5MW planned**. The pattern holds across the moratorium map: these measures land overwhelmingly in inconsequential areas, or if not, the projects were already too early stage for 2026 anyway.
